

Construction Update

February 14, 2020

Numbers as available at the end of January 2020

Coastal GasLink Pipeline Project

Construction highlights

Construction of a natural gas pipeline project involves more than stringing together pieces of pipe. A lot of additional infrastructure is needed, from laydown and storage areas for equipment and construction staging, to the lodges needed to house the approximately 2,500 women and men who will build the project.

Many of these workforce sites – or lodges – are built and housing workers today, others are under construction for a later stage of project construction. But all of them are being constructed and operated in partnership with Indigenous communities along the 670-kilometre project route.

A great example is Little Rock Lake Lodge, which opened in late 2019. You can learn about this unique workforce accommodation site and history through a [video](#) that was recently launched following the ceremonial opening

of the Lodge together with the Nadleh Whut'en and Stelat'en First Nations. The Lodge is open today and will eventually house up to 700 women and men working on Coastal GasLink at peak construction.

We also require areas to store and stage our equipment and the materials needed to assemble the natural gas pipeline. Currently, pipe segments are arriving across the project route and being stored at designated storage sites until they are needed when pipe assembly commences later this year.

All of these activities are generating jobs for many Indigenous and local workers from communities along the project route. Currently, more than 1,200 women and men are working — this number will continue to increase as clearing activities continue and mainline construction commences.

Performance at a glance:




46%
of route cleared



1,235

workers at accommodation sites (approximately)

**Occupancy rates subject to fluctuation*

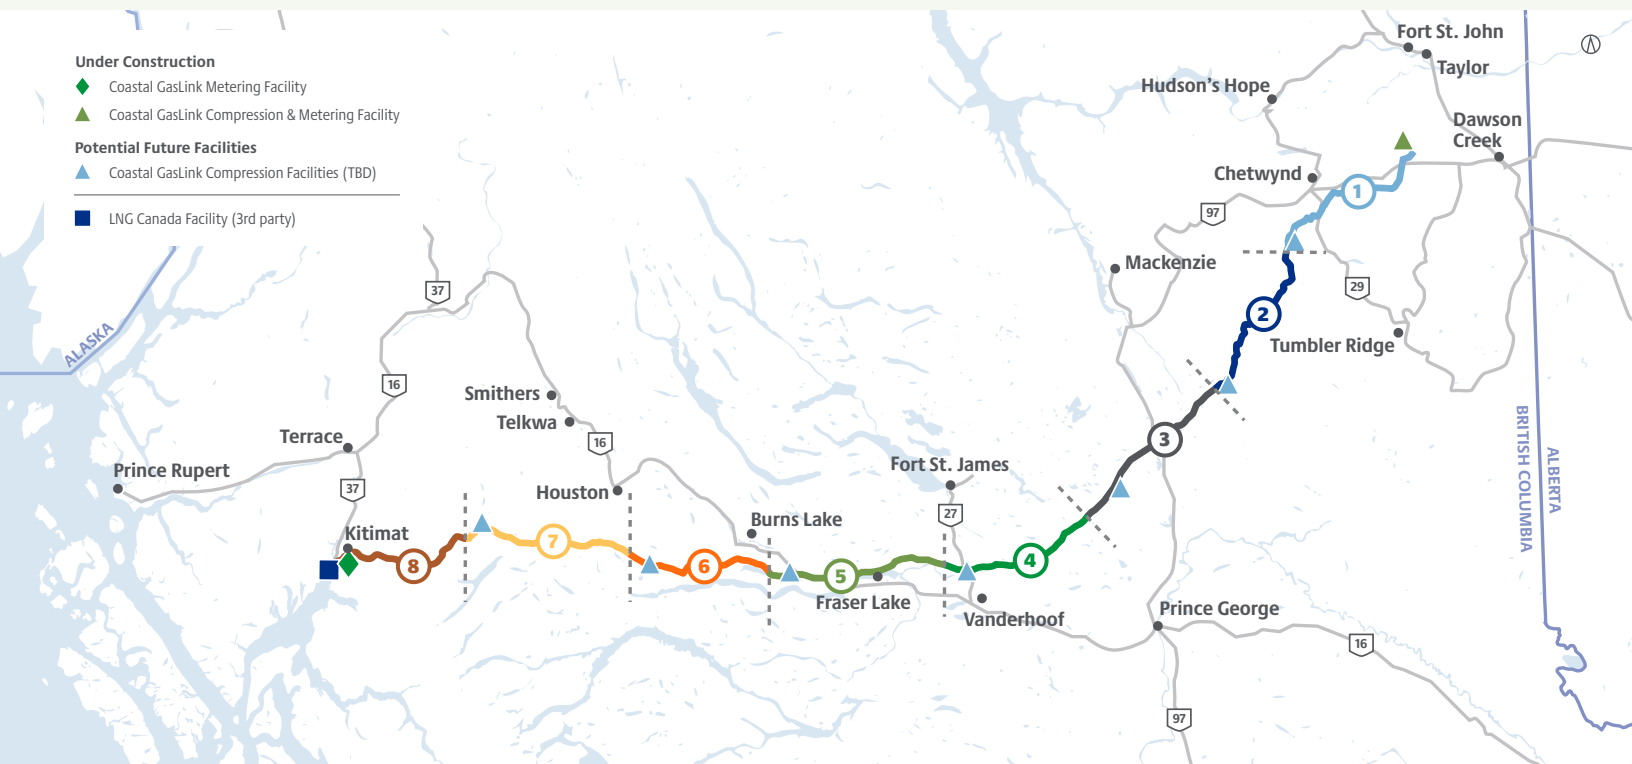

1 Section 1: Monthly Construction Update

Performance at a glance:



62%
of route cleared



Chetwynd Lodge
accommodation site
under development

Section 1


Location: West of Dawson Creek to south of Chetwynd

Length: 92 kilometres

Prime Contractor: Surerus Murphy Joint Venture

Workforce Accommodations: One Workforce
Accommodation – Chetwynd Lodge

- Project Right-of-Way (Section 1)
- Workforce Accommodation Site
- Storage Area (Where construction equipment and materials are stored)
- Kilometre Post Markings (KP)

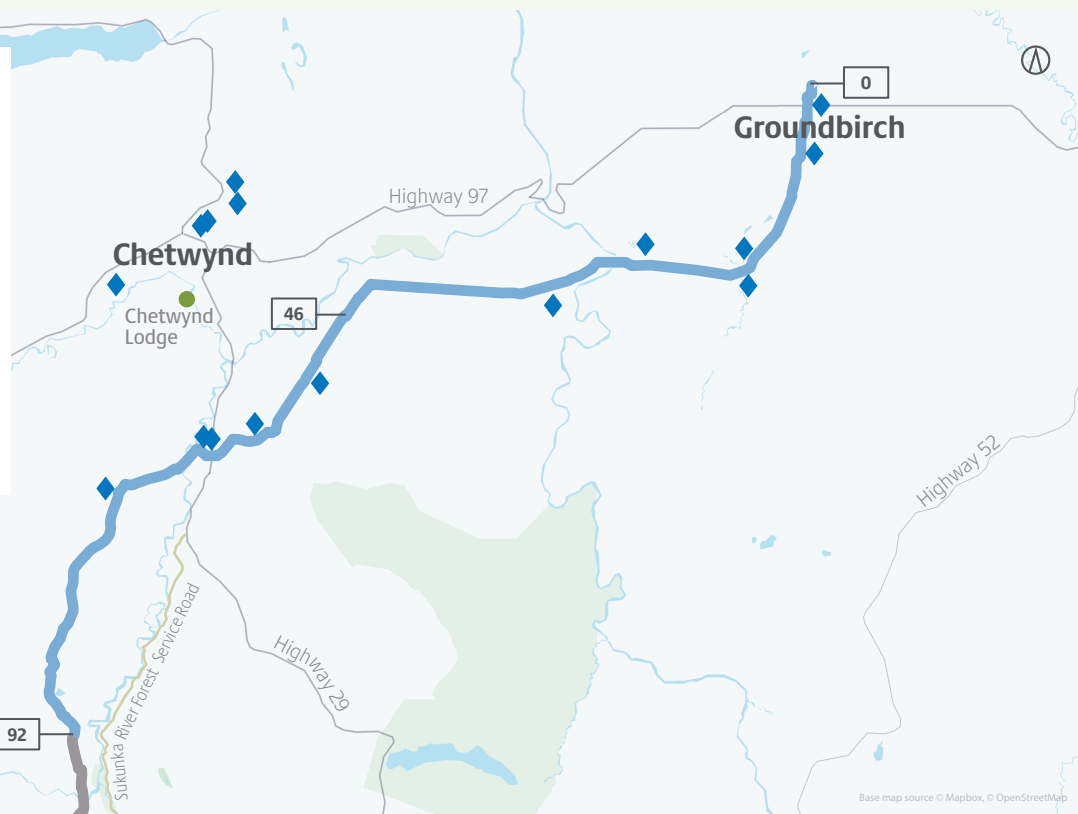

Construction progress:

- Cleared an additional 9% of the right-of-way in the past month
- Commenced blasting right-of-way south of Chetwynd
- Continued road and bridge upgrades
- Delivered 15 km of pipe to storage areas

Upcoming activities*:

- Continue clearing of right-of-way
- Burning of vegetative matter such as non-merchantable trees as required by right-of-way conditions
- Blasting activities continuing as required by right-of-way conditions
- Drone surveys to assess clearing and grading activities continue into May, 2020
- Pipe deliveries continue in the Chetwynd area until May, 2020

**All schedules are subject to change*

Did you know?

Coastal GasLink is employing drones to survey route topography for clearing activities. Drones provide an efficient and unobtrusive way to view the project corridor. Including conditions and terrain. All drone operations will be in accordance with provincial and federal regulations.

② Section 2: Monthly Construction Update

Performance at a glance:



37%
of route cleared



213
workers at Sukunka Lodge

Section ②


Location: South of Chetwynd to east of McLeod Lake

Length: 48 kilometres

Prime Contractor: Surerus Murphy Joint Venture

Workforce Accommodations: Two Workforce Accommodations – Headwall Lodge and Sukunka Lodge

- Project Right-of-Way (Section 2)
- Workforce Accommodation Site
- Storage Area (Where construction equipment and materials are stored)
- Kilometre Post Markings (KP)

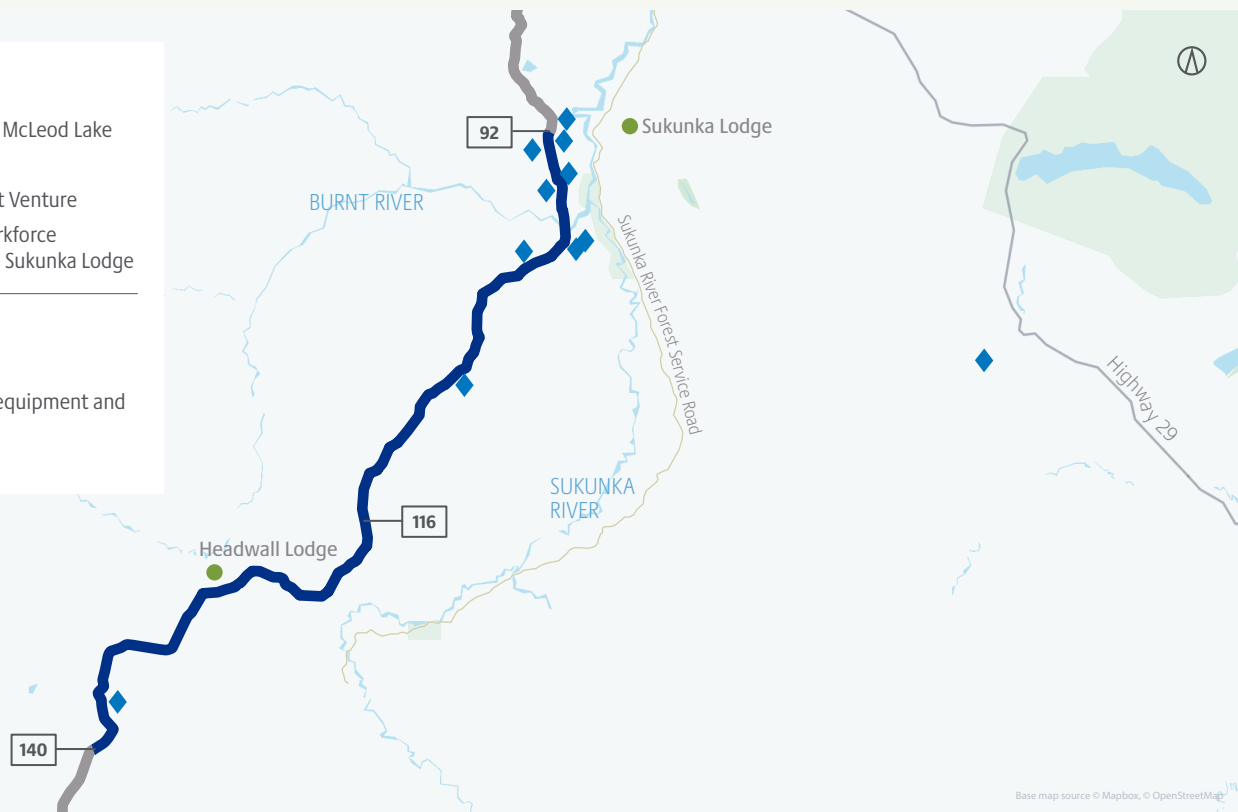

Construction progress:

- Cleared an additional 13% of the right-of-way in the past month
- Continued road and bridge upgrades along the route including road brushing to decrease the height of vegetation to maintain a safe line of sight
- Delivered 7 km of pipe to storage areas

Upcoming activities*:

- Continue clearing of right-of-way
- Burning of vegetative matter such as non-merchantable trees as required by right-of-way conditions
- Blasting activities continuing as required by right-of-way conditions

**All schedules are subject to change*

3 Section 3: Monthly Construction Update

Performance at a glance:



52%
of route cleared



340
workers at Parsnip Lodge

Section 3


Location: East of McLeod Lake to north of Prince George

Length: 104 kilometres

Prime Contractor: SA Energy Group

Workforce Accommodations: One Workforce Accommodation – Parsnip Lodge

- Project Right-of-Way (Section 3)
- Workforce Accommodation Site
- ◆ Storage Area (Where construction equipment and materials are stored)
- Kilometre Post Markings (KP)

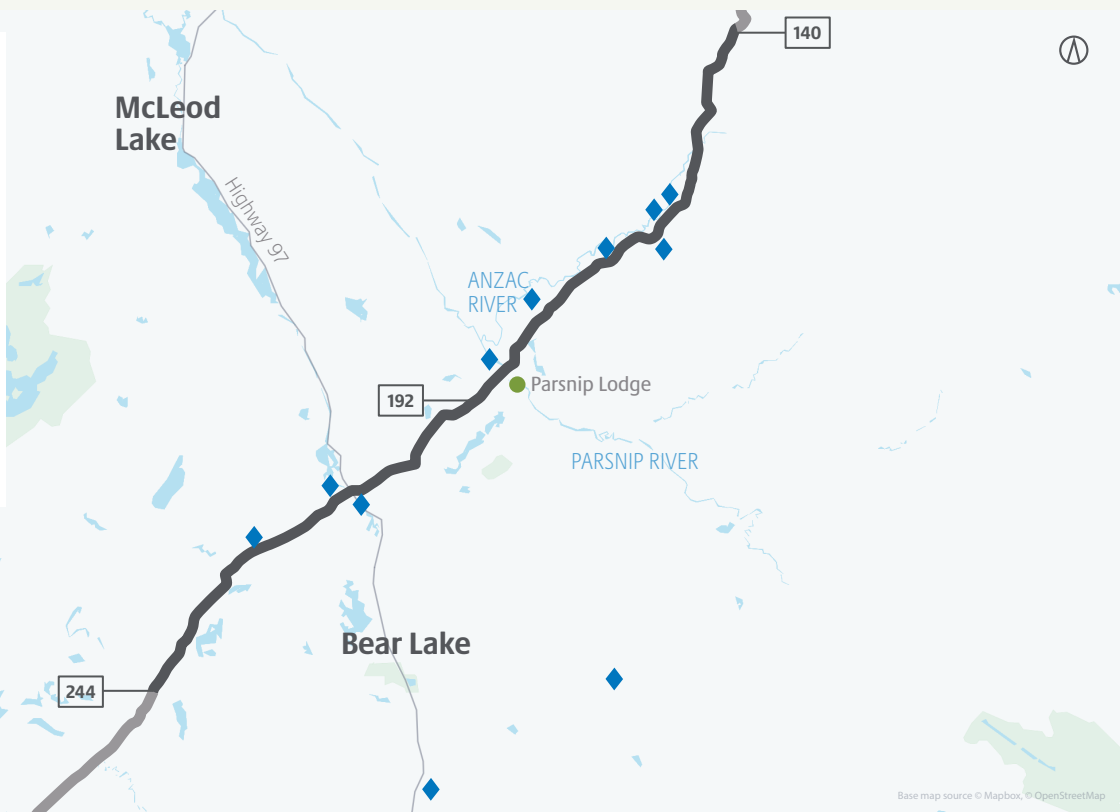

Construction progress:

- Cleared an additional 9% of the right-of-way in the past month
- Continued road and bridge upgrades along the route, including road brushing to decrease the height of vegetation to maintain a safe line of sight
- Pipe deliveries continue in the Prince George area with 41 km of pipe now stockpiled at Section 3 storage sites

Upcoming activities*:

- Continue clearing of right-of-way
- Blasting activities continuing as required by right-of-way conditions
- Pipe deliveries continue to storage sites in Section 3 until April, 2021

**All schedules are subject to change*

④ Section 4: Monthly Construction Update

Performance at a glance:



76%
of route cleared



106
workers at 5B Lodge



Construction progress:

- Cleared an additional 28% of the right-of-way in the past month with workers at 5B Lodge, a temporary workforce accommodation site in use until end of February to assist with Section 3 and 4 clearing

Upcoming activities*:

- Continue clearing of right-of-way
- Burning of vegetative matter such as non-merchantable trees as required by right-of-way conditions
- Continue development of access roads

**All schedules are subject to change*

5 Section 5: Monthly Construction Update

Performance at a glance:



57%
of route cleared



162
workers at Little Rock Lake Lodge

Section 5

Location: North of Vanderhoof to south of Burns Lake

Length: 82 kilometres

Prime Contractor: Macro Spiecapag Joint Venture (MSJV)

Workforce Accommodations: One Workforce Accommodation – Little Rock Lake Lodge

- Project Right-of-Way (Section 5)
- Workforce Accommodation Site
- Storage Area (Where construction equipment and materials are stored)
- Kilometre Post Markings (KP)



Construction progress:

- Cleared an additional 29% of the right-of-way in the past month, with 81 more workers at Little Rock Lake Lodge

Upcoming activities*:

- Continue clearing of right-of-way
- Pipe deliveries to area storage sites to commence April, 2020

**All schedules are subject to change*

6 Section 6: Monthly Construction Update

Performance at a glance:



3%
of route cleared



7 Mile Road Lodge accommodation site under development; 140 workers currently residing in Burns Lake area

Section 6

Location: South of Burns Lake to south of Houston

Length: 85 kilometres

Prime Contractor: Pacific Atlantic Pipeline Construction Inc. (PAPC)

Workforce Accommodations: One Workforce Accommodation – 7 Mile Road Lodge

- Project Right-of-Way (Section 6)
- Workforce Accommodation Site
- Storage Area (Where construction equipment and materials are stored)
- Kilometre Post Markings (KP)



Construction progress:

- Continued preparations for right-of-way clearing with clearing now underway
- Ongoing preparation of 7 Mile Lodge site setup
- Ongoing road upgrades and maintenance activities

Upcoming activities*:

- Continue clearing of right-of-way
- Continue road upgrades and maintenance activities
- Preparations for 7 Mile Lodge underway for an anticipated opening in March, 2020

**All schedules are subject to change*

Did you know?

Road safety is a critical part of our legacy. Learn about Coastal GasLink's Safe Driving Guidelines in our newest **Coastal GasLink Connector**.

7 Section 7: Monthly Construction Update

Performance at a glance:



0%
of route cleared



Preparing for development of
Huckleberry Lodge site

Section 7

Location: South of Houston to north of Morice Lake

Length: 78 kilometres

Prime Contractor: Pacific Atlantic Pipeline Construction Inc. (PAPC)

Workforce Accommodations: One Workforce Accommodation – Huckleberry Lodge

- Project Right-of-Way (Section 7)
- Workforce Accommodation Site
- ◆ Storage Area (Where construction equipment and materials are stored)
- Kilometre Post Markings (KP)



Construction progress:

- Continue development of Houston area pipe storage site with anticipated pipe delivery starting in February, 2020
- Continue preparations for clearing and grading at the Huckleberry Lodge site

Upcoming activities*:

- Commence clearing and grading at Huckleberry Lodge
- Conduct survey and field environmental studies
- Pipe to arrive at Houston storage site beginning February, 2020 until April, 2021

**All schedules are subject to change*

8 Section 8: Monthly Construction Update

Performance at a glance:



63%
of route cleared



274
workers at Sitka Lodge

Section 8

Location: North of Morice Lake to Kitimat

Length: 84 kilometres

Prime Contractor: Macro Spiecapag Joint Venture (MSJV)

Workforce Accommodations: Seven Workforce Accommodations


– Sitka Lodge, Hunter Creek Lodge, Icy 1 Lodge, Icy 2 Lodge, P2 Lodge, 9A Lodge, P4 Lodge

— Project Right-of-Way (Section 8)

● Workforce Accommodation Site

◆ Storage Area (Where construction equipment and materials are stored)

□ Kilometre Post Markings (KP)

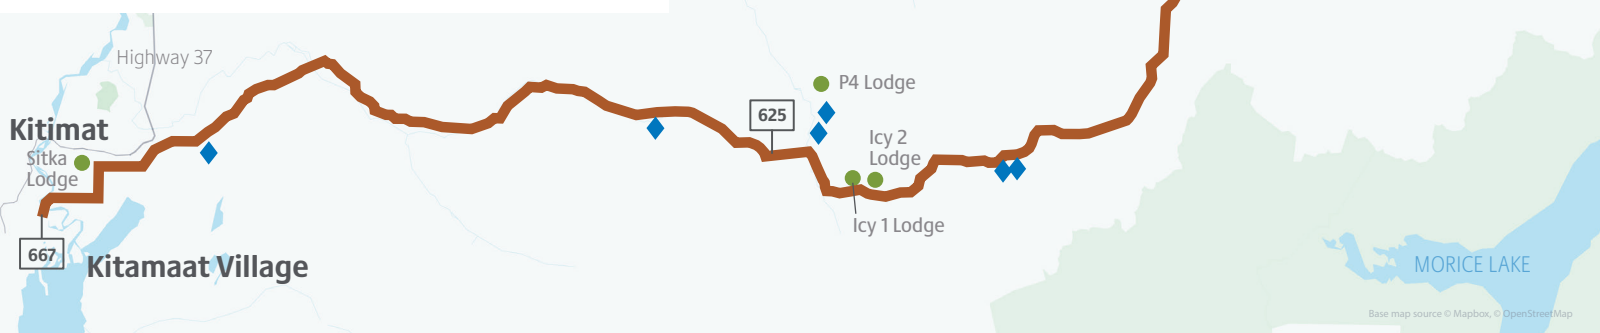

Construction progress:

- Cleared an additional 11% of the right-of-way in the past month

Upcoming activities*:

- Blasting activities continuing as required by right-of-way conditions
- Continue receipt of pipe to North Kitimat storage areas
- Commence expansion of Hunter Creek and 9A Lodges, and preparation for P4, Icy 1, and Icy 2 Lodges
- Continue clearing works to extent possible for remainder of the construction season
- Pipe deliveries continue in the Kitimat area until April, 2021

**All schedules are subject to change*



Photo of the month

7 Mile Lodge under development

The 7 Mile Lodge is under development in Section 6. The lodge will accommodate up to 580 workers between February, 2020 to May, 2021, and is being developed in partnership with the Wet'suwet'en First Nation, Ts'il Kaz Koh First Nation (Burns Lake Band), YLP-Civeo and Summit Camps.



About Coastal GasLink's Construction Updates

Our construction updates include information on recent progress, activities that we expect over the next month, and detailed section maps that help communicate where project infrastructure is located and where activities are happening.

Check us out!

We've updated **CoastalGasLink.com**! Find information, such as Construction Updates and an interactive map, under Construction, and tour the site to find details on economic benefits and employment contacts.

Keep in touch and learn more

We want to make sure you have access to the information you need about the project. Here are the many ways you can reach out, and learn more:



Visit our website:
CoastalGasLink.com



Follow us on Facebook:
@CoastalGasLink



Sign up to receive our Connector Newsletter: **CoastalGasLink.com/contact**



Email us:
coastalgaslink@tcenergy.com



Follow us on Twitter:
@CoastalGasLink



Visit our community office:
Prince George
760 Kinsmen Place

Coastal GasLink
Pipeline Project

